Project plan

Authors	Kamiel de Visser (500838438), Lisanne van Vliet (500816952), Mathijs Marks (500761805), Sarah Rehman (500798305) and Timber Rijsdorp (500828963)
Team	IVMD1 Wortell
Subject	Project Mobile Development
Teacher	Hans Twelker
Date	23 February 2020
Version	1.0

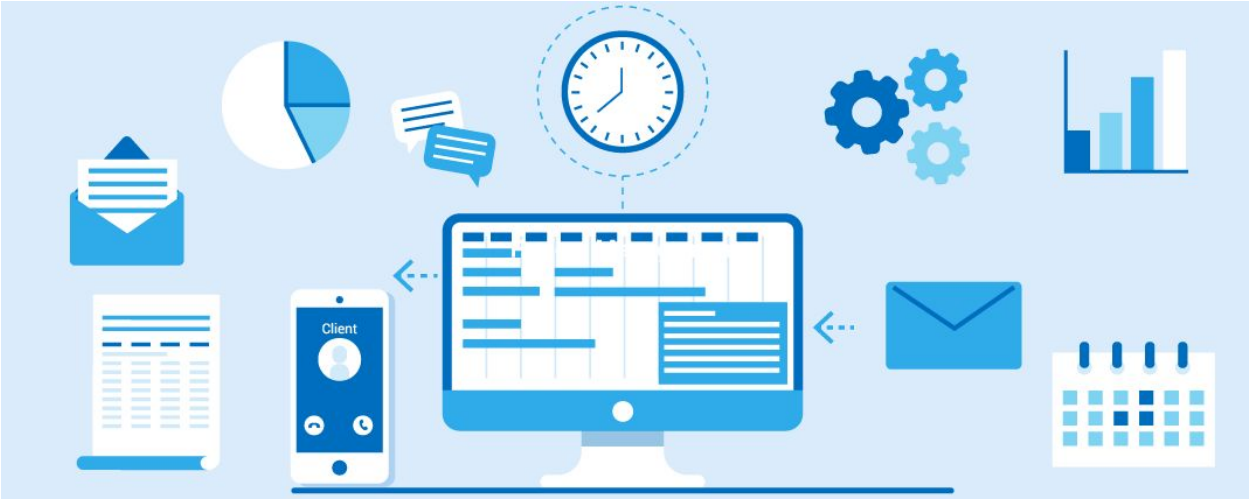

Table of contents

Background 3

Objectives 3

Deliverables 3

Scope 4

Organization 5

Project approach 6

Planning 6

Communication 7

Time management 7

Quality control 8

Risks 8

Background

Wortell has a Managed Detection and Response service and is a 24/7 cybersecurity service for securing our IT environments. They provide insight into the risks you run in the field of cybersecurity, and take immediate action when a threat is active in your IT environment.

Every incident that they detect is followed up through tasks. Each task concerns an activity that contributes to resolving the incident. For the task 'Validate with customer' they want to develop an app where the request for validation can be sent to the relevant customer contact by means of push messages.

They therefore want to have an application developed that can be used by our MDR customers to follow up security incidents.

Objectives

The main goal of this project is to make a smartphone app that gives a notification to the user when a suspected security risk or breach has found place. Objectives that can achieve this goal are:

- The app works for both Android and IOS.
- The app will determine if the security risk or breach is urgent.
- If there is an urgent security risk or breach, the app will send a notification to the user.

Deliverables

General deliverables:

- 19 February 2021
    - Collaboration Agreement
    - URL of Team site
    - Timesheet
    - Name of Team leader
    - Project plan
- 12 March 2021
    - Individual learning report
    - Legal contract
- 12 April 2021
    - Product demo
- 23 April 2021
    - Midterm self-reflection

- 11 June 2021
    - Individual learning report
    - Final including self-reflection
- 21 June 2021
    - Final presentation and demo

Product deliverables:

Functional requirements:

Non-functional requirements:

Scope

The Product deliverables are an important part of the project. These deliverables are the requirements of the product that we have to make in this project. These requirements define what the product owner expects and wants from us in this project.

The deliverables that have to be made before the 19th of February are deliverables that help us prepare for the project. These deliverables include things like an Collaboration Agreement, Team site, Timesheet and this project plan. With these deliverables we have an understanding how the project and team will work.

We have two product demos during this project including the final demo. During these demos we will show our product and the progress we have made. At the final demo we will have to show our definitive product for this project.

We also have to make Individual learning reports and self-reflections. These assignments are mainly important to the school, so that they know what we have learned and how we are improving in this project. Every team member has to make these assignments to reflect on his/her work during the project.
Finally we have to make retrospectives after each sprint/cycle. In these retrospectives we have to reflect as a team what went right, what went wrong and what we can do to improve in further sprints.

Organization

Hans Twelker
School contact person - Responsible for providing us the contact details of the external company (Wortell). Besides that he will be grading our entire project for a total of 12 study points.

Jair Hokstam
Wortell contact person - Responsible for providing an assignment where the team can work on during this semester. Next to that he takes care of the administration and setting up contact with our product owner and developer who is gonna assist us with the project.

Jeroen Niesen
Product owner - Responsible for defining stories and prioritizing the team backlog to streamline the execution of program priorities while maintaining the conceptual and technical integrity of the feature or components for the team. Besides that he leads the daily stand-up every tuesday and wednesday.

Maurice de Jong
Developer - Responsible for helping us with our technical issues and questions. Besides that if we need some training or help regarding the project we can come to him.

Lisanne van Vliet
Team leader - Responsible for the end product, the contact with the client and the dynamics within the team.

Kamiel de Visser
Gitlab administrator - Responsible for the layout of our GitLab repository. (Approve) merge requests, provide clear branches, etc.

Mathijs Marks
Note taker - Responsible for taking care of the minutes on the project working days (Tuesdays and Wednesdays). In addition to noting down important matters, the secretary is also responsible for keeping time during the meetings. After each meeting, the secretary works out the minutes further and reminds the team members of the agreements made.
In addition to taking minutes, also supports the Team Leader in her duties and is present at the meetings with the contact person of Wortell.

Sarah Rehman
Secretary - Responsible for making the planning, including the deadlines for the project as own set deadlines. Also actively send reminders to team members every week. Besides that the responsibility for managing all our documents in Google Drive**.**

Timber Rijsdorp
Scrum master - Management of user stories in the backlog and distribution of these stories in the sprints. Responsible for the description, definition of done, Scrum points and other parts of user stories.

Project approach

Give an outline of the methods that are going to be used during the project. Break down the project into meaningful stages or, when using an agile development method, sprints. Identify milestones.

- Agile development
- Azure dev-ops

Planning

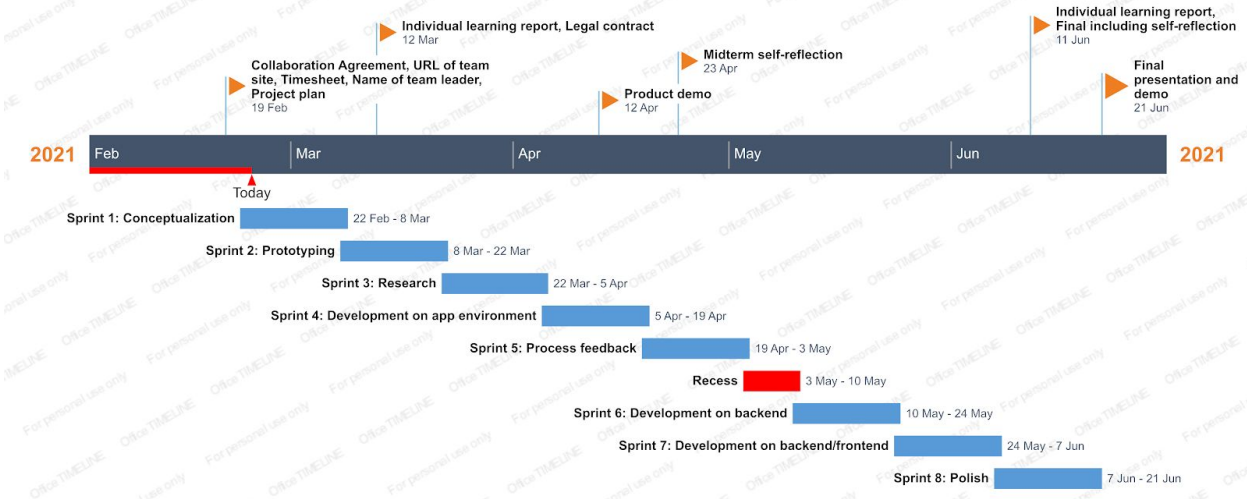

Communication

The communication with stakeholders will be organized by having a stand-up every morning on Tuesday and Wednesday. During the standup, we will discuss the progress made, the problems we encountered and the goals for the sprint. This standup will take place in Microsoft Teams, with the product owner Jeroen. We also communicate by email, to schedule meetings and the corresponding agenda. Jaïr will be our contact who oversees the whole project. For technical questions, we will contact Maurice, the technical expert of our project.

Another stakeholder is Hans Twelker, the teacher of Project Mobile Development. On Mondays, Hans will ask us how the project is going. We can always contact him by email or Microsoft Teams, for questions about deadlines or problems within the team.

The team communication will be organized by holding a Discord voice call on Tuesday and Wednesday. Each week, we will agree upon internal deadlines, which are a bit earlier than the official ones. This way, we ensure that we have so-called *slack* in our planning, so that we do not miss a deadline if unforeseen circumstances arise, such as a sick teammate. Aside from Discord, we also have a group chat on WhatsApp, in which we communicate absences, plan internal meetings, and other general communication.

Time management

Since the team will be working with Agile, time management will be based on the Scrum method. This means that the team will be planning and working in sprints of **two weeks**.
Each sprint starts with a sprint planning where the team picks the required tasks from the backlog. Then the team can start working on a Minimum Viable Product (MVP). At the end of each sprint, this product is presented to the Product Owner in a sprint review. This short cycle repeats itself for 8 sprints until the final product can be presented.

During the sprint, the team will gather on Tuesdays and Wednesdays to work on the project. At the start of each project day, the team will gather with the Product Owner for a standup. In this standup the team will briefly discuss their plans for today, express what they need to execute said plans, and discuss any possible difficulties/problems they think they might encounter.

At the end of the project day, the team will gather again for a stand down where the team will discuss progress made through the day, as well as any problems they encountered. With this information, the planning for the next project day can be scheduled.

In order to work with this method, a few tools are required:

- **Azure Boards** for managing backlog and sprints.
- **Clockify** for time tracking.
- **Teams** for scheduling meetings with HvA (University) and Wortell (External company).
- **Google docs** for keeping meeting records. Within these records an Action Plan is included where internal deadlines for each meeting can be recorded.
- **Discord** for notifying team members of upcoming deadlines through the #deadlines text channel.

Quality control

What quality criteria are already known? How will the (technical) quality of products be managed during the project?

- Code needs to be manageable and follow (to be determined) coding standards
- We'll use code quality
- Needs to be secure
- Needs to run on both Apple and Android mobile devices
- Needs to adhere to the design standards set by Apple / Android
- Needs to adhere to the legal requirements set by Apple / Android

Risks

Despite careful planning and documentation, there's still risks involved when working on this project. As with each project, measures need to be made to mitigate said risks and deal with any events that might threaten the project.

Common risks that can include in this project are:

- **Schedule risk**
  Poor time estimates and planning can result in tasks, or even sprints, taking longer to complete than expected. This may force the team to lower the scope of the project in order to catch up, which lowers the quality of the end product.
- **Performance risk**
  No matter the results the team can deliver to the project, there's always the risk that the product ends up not performing to the user's needs. This can happen even when the team performs at its best. The best way to deal with this is to stick to the schedule and to not develop more than is needed.
- **Operational risk**
  Another risk that can happen is the team having process or implementation related issues. Because of this the team may end up developing a solution that did not meet the expectations of the project managers. By keeping clear communication between the parties (Team, project managers, clients) and sticking to the schedule, this risk can be mitigated.
- **Legal risk**
  A legal risk can include one or more team members breaking their NDA or other signed contracts.
- **External hazard risks**
  External risks can include a team member falling ill or otherwise experiencing an event that would deem them unable to continue working on the project.
